

ORDER FORM

CALIDRIS MTM SILESTONE/DEKTON WORKTOPS

Customer:	Required supply date: (min. 6 weeks)	Order no./Ref.:
Contact person:	Order date:	Order no. Dansani: (added by Dansani)


Silestone® decor See available colours on our website		Dekton® decor See available colours on our website	
Silestone® surface	Suede	Polished	
Worktop size max measure 2405 mm x 600 mm Width _____ mm Depth _____ mm			

Cutouts - for countertop basins (Depth 405 mm without tap hole, 505 mm with tap hole)
 Tick the box(es) where taphole(s) are required.


☐ Globe
☐ Orbit

☐ Ellipse
☐ Cosmo

☐ Without tap hole

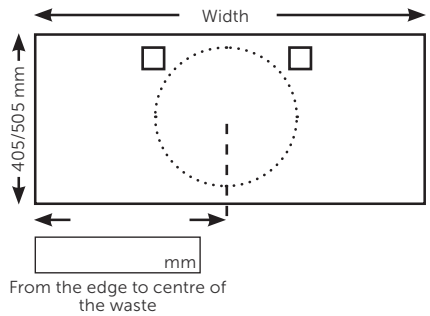


1 x cut-out UD1

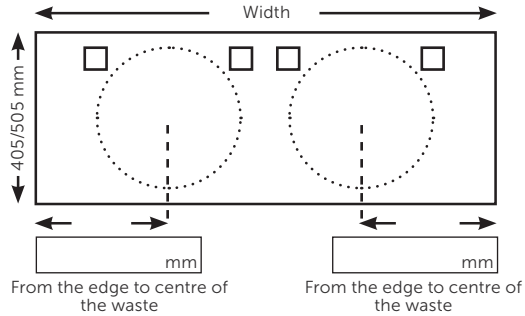

2 x cut-outs UD2

Item no. for cut-out(s) for countertop basin(s) at additional cost. See catalogue for prices:

Accessories: Basin waste with automatic opening at additional cost. See catalogue for prices.		Chrome Art. no. 4884343	Polished brass Art. no. 4884344	White matt Art. no. 4884310	Black Art. no. 4884328
--	---	----------------------------	------------------------------------	--------------------------------	---------------------------

NB:

- Product design requires the support of a vanity unit below the worktop.
- The worktops have a tolerance of +1/-1 mm; we recommend that all worktops are ordered 5 mm wider than the furniture setting (e.g. 1605 mm total width to suit 2x800 mm units).
- Centre of the countertop basin must be aligned with the centre of the vanity unit.
- For wall-to-wall solutions we recommend 3 mm space on both sides between worktop and wall. Take care to note the diagonal measurement between the walls.

- All worktops are supplied as standard without a tap hole unless otherwise specified. Customer specific placement of the taphole must be specified with measurements from the wall (back edge) and centre of basin, including diameter. This is at the customer's own risk.
- Bespoke products cannot be **changed**, cancelled or returned after the signed order form is received.
- Please be aware that the warranty no longer applies if modifications to the construction and/or the design are carried out.

Signature of acceptance Name/Company stamp
--
